





QUARTERLY PROGRESS REPORT FOR BADAMPAHAR AREA DEVELOPMENT


YMSCE-PRJ17006-PR-006



SLS Trust

OCT to DEC 2022






YMS Consulting Engineers

502, Thawar Apartment,
Above Canara Bank, Main Carter Road
Borivali (E), Mumbai 400 066
Phone: +91 90821 87165

Rev	Date	Description	Made by	Chkd by	App by
R0	Jan 10, 22	First Issue	MSB	SAB	YMS
<input checked="" type="checkbox"/>	Entire Specification	DOCUMENT ISSUED FOR			
	Issued this Revision	<input type="checkbox"/>	In-house Review and replies	<input type="checkbox"/>	Purchase
<input type="checkbox"/>	Revised Pages Only	<input type="checkbox"/>	Client Approval	<input checked="" type="checkbox"/>	Publishing
	Issued this Revision	<input type="checkbox"/>	Enquiry	<input type="checkbox"/>	Engineering



Index

1.0	Executive Summary	5
2.0	Infra Development Status	5
2.1	Consultant Details for Infrastructure.....	5
3.0	Construction Status	5
3.1	Progress till Dec 2022.....	5
3.2	Progress till Dec 2022.....	6
3.3	Other Initiatives.....	6
3.4	Brief on 1 st batch result of class 10 th	6
4.0	Pending / Open item list/ Hold up items	6
5.0	New initiative	7
6.0	Look Ahead plan for Q3 - 2022	7
7.0	Support Provided	7
8.0	Support Needed EDCIL and CSC	7
9.0	School Plan.....	8
11.0	Site Progress Photos	9

This document has been prepared for the above project or named part thereof and should not be relied upon or used for any other project without prior written consent from YMS Consulting Engineers. YMS Consulting Engineers accepts no responsibility or liability for the consequence of this document being used for a purpose other than the purposes for which it was commissioned. Any person using or relying on the document for such other purpose agrees, and will by such use or reliance be taken to confirm his agreement to indemnify YMS Consulting Engineers for all loss or damage resulting there from YMS Consulting Engineers accepts no responsibility or liability for this document to any party other than the person by whom it was commissioned.

Index of Figures

Figure 1: Revised School Plan.....	8
Figure 2: One of the 5G Launch Center by. Hon PM has dedicated to the country	9
Figure 3: 5G Center Launch.....	9
Figure 4: 5G Center Launch.....	10
Figure 5: 5G Center Launch.....	10
Figure 6: First Santali Wall Painting	11
Figure 7: First Santali Wall Painting	11
Figure 8: Festival Celebration	12
Figure 9: Festival Celebration	12
Figure 10: Children's Day Observation	13
Figure 11: Children's Day Observation	13
Figure 12: Children's Day Observation	14





Figure 13: Children's Day Observation 14



1.0 Executive Summary

This is the Fifth (5th) report for the Project and covers the Quarterly period from Oct 2022 to Dec 2022.

SLS Trust works for the welfare of the children, aged men and women by undertaking different development rehabilitation program of the government as well as provide local aid to them.

With this aim, the trust has explored possibility of running a school SLS Memorial Residential School to spread the ideals for human life, such as educational, Arts, Culture, Yoga and Value based basic education for the achievement of perfect human being and perfect society. One of the objectives of setting up the school and other social engineering programs is to encourage skill development which is so crucial to the growth of the region.

With this intention they intend to undertake the construction of the basic infrastructural facilities required for school in the area at Pahadpur, Badampahar, Dist Mayurbhanj, Odisha. Along with this school some other social engineering programs are also being conducted in this area. The pre-construction design activity for the school design has been earlier initiated and completed in the month of December 2017. The Trust has initiated the next phase of construction for building the school classrooms, Office building, additional hostel facility.

2.0 Infra Development Status

Following Consultants are on board for the project and the Consultants designs are in various stages of progress as per details given below.

2.1 Consultant Details for Infrastructure

For the school, Architects and Engineers have been selected and their details are as follows:

Sr. No.	Discipline	Organization
1.	Overall Management	SLS Trust
2.	Architect	YMS Consulting Engineers, Mumbai
3.	Civil and Structural Engineers	YMS Consulting Engineers, Mumbai
4.	MEP Engineers	YMS Consulting Engineers, Mumbai
5.	Project Coordinator	Mr. Subodh Kumar


3.0 Construction Status

3.1 Progress till Dec 2022

All the Architectural, Civil and Structural Designs were complete. Subsequently the plans had to undergo revision on account of the land area and the existing structures.

- Temporary 4 Nos. Class room
- Boundary Wall
- Kitchen Construction completed
- Girls and Boys hostel for total 80 students
- Drinking Water facility
- Permanent 5 Nos. Class room

There are many other facilities which are planned for the students of this school. These facilities will help the students in their academic activities, whereby imparting continuing improvement in the students. These facilities are as follows:



- a. Library / Study room
- b. Laboratory
- c. 3 Nos. Permeant Class room
- d. Enhancing Girl and Boys hostel
- e. Smart board Class Room
- f. Computer Lab
- g. Computer added van

For the construction and mobilization of the above facilities, support is being solicited from various organizations, for their financial assistance, to enhance the quality of education at this schooling institutions

3.2 Progress till Dec 2022

In this phase, the following have been constructed:

- a. Dining Hall Construction has started

The further construction work is now planned and being started.

3.3 Other Initiatives

The following initiatives which were started in the earlier quarters were completed.

- a. Skill development classes for Electrical Technician were started as per industrial need this quarter. This has provided new skills to the local youth who will now be better equipped for the future opportunities.

3.4 Brief on 1st batch result of class 10th

From the time the school has started academic operations, many students have enrolled at this institution. The teachers and instructors at this school have helped numerous students with their teaching. This structured schooling has helped the students, in their upliftment, by making them academically qualified individuals in this society. This will also assist the students to enter into the society, as educated and literate individuals.

Continuing the trend of education at this institution, it is with great pride to note that the first batch of Standard 10th students from the SLS School have recently passed out from this institution.

A brief update on the 1st batch result of class 10th of SLS school is as follows:

Sr. No.	Student Passing	Number
1.	Total Number of Students	15
2.	Students passing in 1 st Division with Distinction	7
3.	Students passing in 1 st Division	3
4.	Students passing in 2 nd Division (above 56%)	5

The positive results indicate that the SLS school is making a big difference to the educational background of the children in this vicinity.

4.0 Pending / Open item list/ Hold up items



- a. Library / Study room
- b. Laboratory
- c. 3 Nos. Permeant Class room
- d. Enhancing Girl and Boys hostel
- e. Smart Class Room
- f. Computer Lab
- g. Computer added van

5.0 New initiative

The following new initiatives were taken up during this quarter:

- a. Skill development courses – Discussion with Various agencies for starting skilled development courses.

6.0 Look Ahead plan for Q3 - 2022

Sr. No.	Activities	Remarks
1.	Library	
2.	Laboratory	
3.	3 Nos. Permeant Class room	
4.	Enhancing Girl and Boys hostel	
5.	Smart Class Room	
6.	Computer Lab	

7.0 Support Provided

The following support was provided by these organizations:

1. IOC / 4 Class room / Completed
2. MCL - 2 Class room and 1 Laboratory – Project sanction
3. SAIL – Girls Hostel - Proposal initiated

8.0 Support Needed EDCIL and CSC

Support from above agencies needed for providing the Digital education.



9.0 School Plan


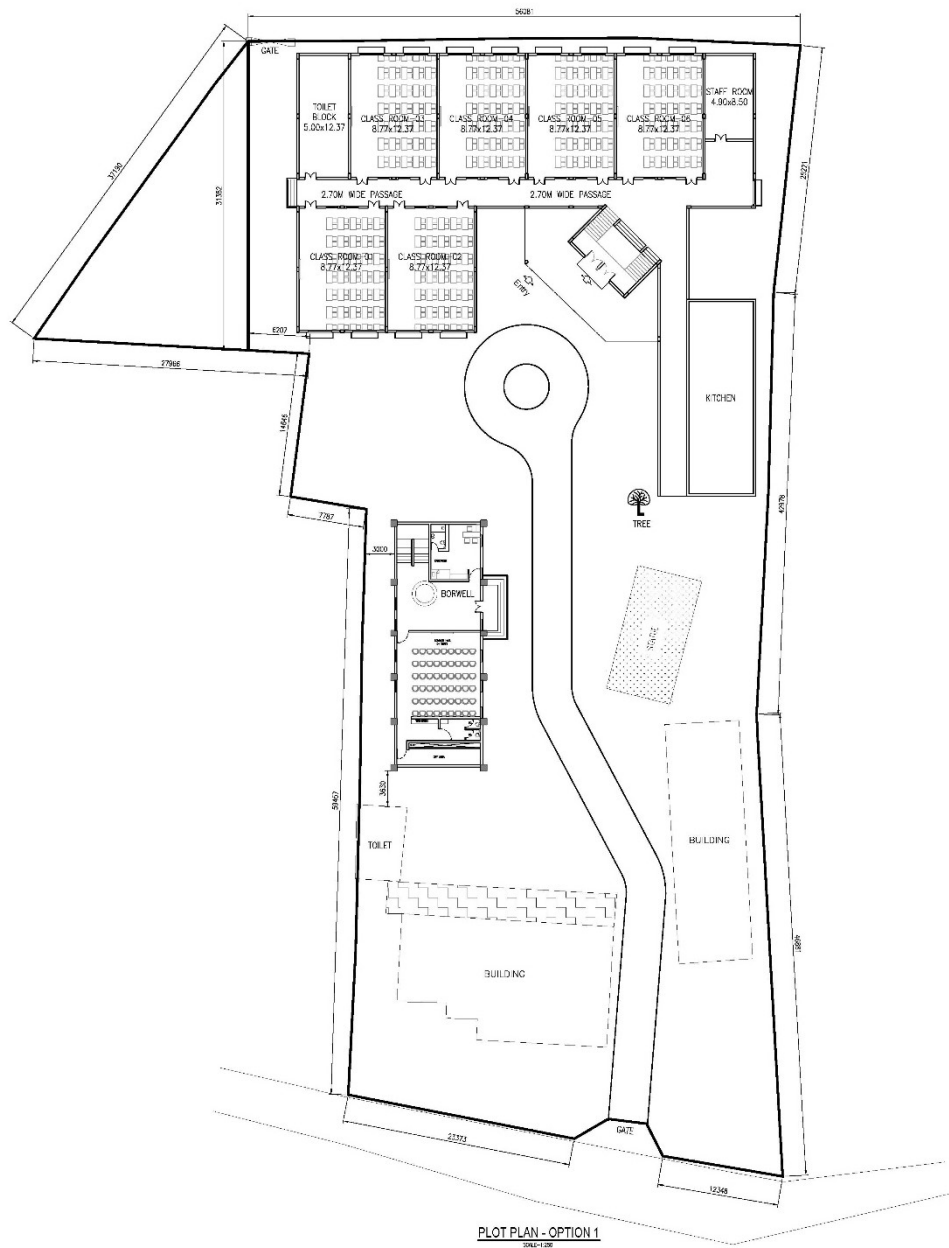


Figure 1: Revised School Plan



11.0 Site Progress Photos



Figure 2: One of the 5G Launch Center by. Hon PM has dedicated to the country



Figure 3: 5G Center Launch




Figure 4: 5G Center Launch



Figure 5: 5G Center Launch




Figure 6: First Santali Wall Painting



Figure 7: First Santali Wall Painting




Figure 8: Festival Celebration



Figure 9: Festival Celebration




Figure 10: Children's Day Observation



Figure 11: Children's Day Observation





Figure 12: Children's Day Observation



Figure 13: Children's Day Observation



Thank You

• End of Document •
